DELAWARE RIVER MAIN CHANNEL DEEPENING

PROJECT SCHEDULE - FEBRUARY 2010

DELAWARE DEEPENING DREDGING CONTRACTS	River Mile	Duration (Mo)	Estimated Quantity (cy)	Dredge	
Contract No. 1 (award year 1)					
Reach C					
C/3 - 192+000 to 206+201 - Killcohook #2	68.3	1.65	932,600	1	HYD
C/2 - 206+201 to 225+000 - Killcohook #3	63.9	2.76	597,800	1	HYD
C/1 - 225+000 to 242+514 - Killcohook #2	60.3	1.38	972,400	1	HYD
Construct Project			2,502,800		
Contract No. 2 (award year 1)					
Reach B - Rock Blasting		3.17		1	BLA
Reach B - Rock Dredging - Fort Mifflin		1.27		1	MEC
Construct Project			77,000		
Contract No. 3 (award year 2)					
Reach AA - National Park		2.88	994,000	1	HYD
19+700 to 32+756	99.2				
Reach A - Pedricktown North		6.10	1,666,600	1	HOP
32+756 to 90+000	96.8				
Construct Project			2,660,600		
Contract No. 4 (award year 3)					
Reach E - Broadkill Beach - Dredge		3.00		2	HOP
461+300 to 512+000	15.6				
Construct Project			1,598,700		
Contract No. 6 (award year 4)					
Reach E - Kelly Island -Dredge		4.50		2	HOP
351+300 to 360+000	36.4		345,800		
360+000 to 381+000	32.1		55,500		
381+000 to 461+300	30.8		2,081,700		
Construct Project			2,483,000		
Contract No. 6 (award year 4)					
Reach D -				1	HOP
249+000 to 270+000 - Reedy Pt. South	55.6	1.13	396,300		
270+000 to 324+000 - Artificial Island	51.8	4.63	1,654,800		
Construct Project			2,051,100		
Contract No. 7 (award year 5)					
Reach B - Oldmans		0.89	1,671,400	1	HYD
Reach B - Pedricktown North		3.51	1,050,700	1	HYD
Reach B - Pedricktown South		0.45	499,300	1	HYD
90+000 to 176+000		2.68	1,443,500	1	HYD
Construct Project			4,664,900		
Total Channel		40	16,038,100		
Berth Deepenings					
Berth Deepenings Drill/Blast					
Berth Deepenings Clamshell					
Berth Deepenings CSD Rehandling WP					
Total Berth Deepenings			450,437		

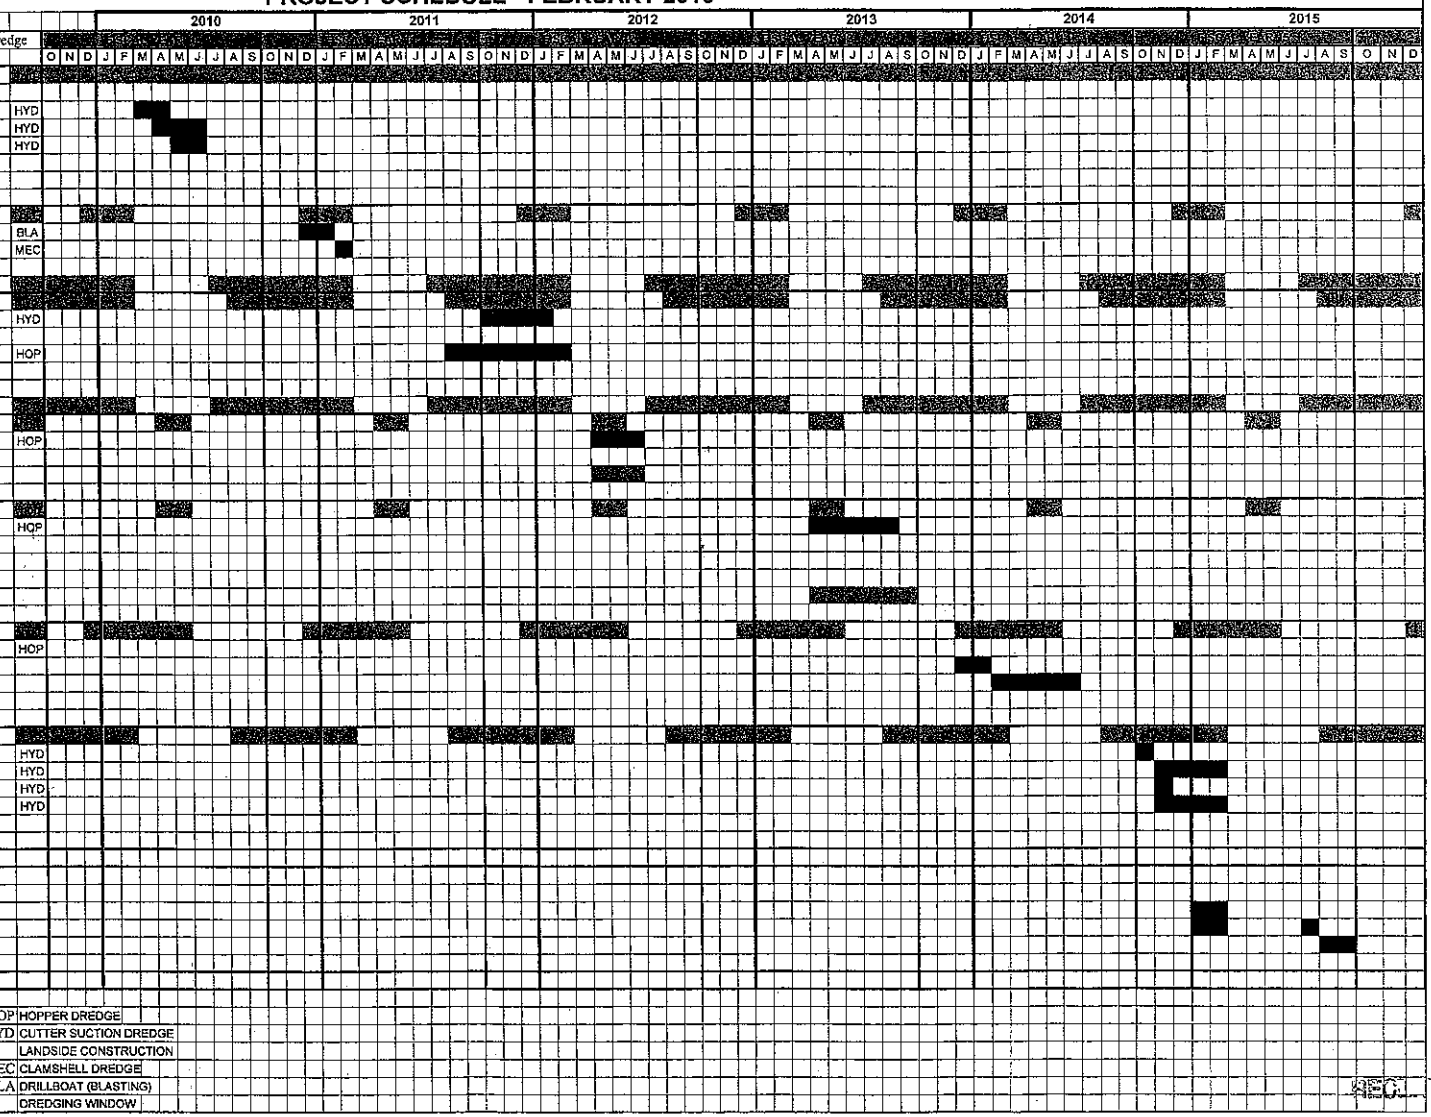

HOP	HOPPER DREDGE
HYD	CUTTER SUCTION DREDGE
	LANDSIDE CONSTRUCTION
MEC	CLAMSHELL DREDGE
BLA	DRILLBOAT (BLASTING)
	DREDGING WINDOW

Revised November 2009

RECEIVED
MAR 22 2010
WETLANDS
