DNREC Division of Watershed Stewardship
89 Kings Highway
Dover, DE 19901
(302) 739-9921

APPLICATION FOR STANDARD PLAN APPROVAL

SIDEWALK, TRAIL, OR OTHER LINEAR IMPERVIOUS SURFACES

Approval of this Standard Sediment and Stormwater Plan may be granted if all of the following criteria are met:

1. Disturbance will be for construction of a sidewalk, trail or other linear impervious surface with total disturbance not to exceed 5.0 acres.
2. No greater than 1.0 acre disturbed at any one time throughout the course of construction.
3. Within the disturbed area, the pre-development land use is not classified as "wooded" based on the 2007 Delaware Land Use/Land Cover data.
4. One of the following is met:
    a. Project site location is within an area previously managed for stormwater quantity and quality under an approved Sediment and Stormwater Plan, AND the post construction condition meets the original stormwater design criteria, or
    b. Comparison of the existing curve number (CN) to the point of discharge as agreed upon with the approval agency, based upon 2007 Delaware Land Use/Land Cover data to the proposed CN to the same point of discharge after sidewalk / trail construction results in less than one whole number change in the CN, or
    c. No new impervious area is proposed as a result of construction.

Site Information

Project Name: _____

Site Location: _____

Previous Plan Name: _____

Previous Plan Approval Number: _____

Tax Parcel ID: _____

Parcel Total Acres (nearest 0.1ac): _____

Disturbed Acres (nearest 0.1ac): _____

Proposed Impervious Area (square feet): _____

Wooded area to be cleared: _____

Pre CN: _____ Post CN: _____

Applicant Information

Owner: _____

Mailing Address: _____

_____

Owner Phone: _____

Applicant: _____

Mailing Address: _____

_____

Applicant Phone: _____

Fees

The review fee is $80 per disturbed acre to the nearest 0.1 acre with a minimum fee of $80 for any standard plan approvals disturbing less than 1.0 acre. Make checks payable to Division of Watershed Stewardship.

Approval Information (for office use only)

Approval # _____ **Fee Paid: $** _____

Approved by: _____ **Approval Date:** _____

Title: _____ **Expiration Date:** _____

Applicant Certification

I, the undersigned, certify that the information supplied on this Application for Standard Plan Approval is accurate, the proposed land disturbing activity meets the criteria established, and all conditions of this Standard Plan Approval will be met by the applicant, builder, contractor, and owner during construction and post construction.

Applicant Signature:_____ Date:_____

Applicant Printed Name:_____ Title:_____

Conditions

1. Impervious surfaces will be graded to sheet flow to lawn or other pervious areas to the maximum extent practicable.
2. Construction site stormwater management best management practices will be used. *Sample best management practices provided in the standard detail below.*

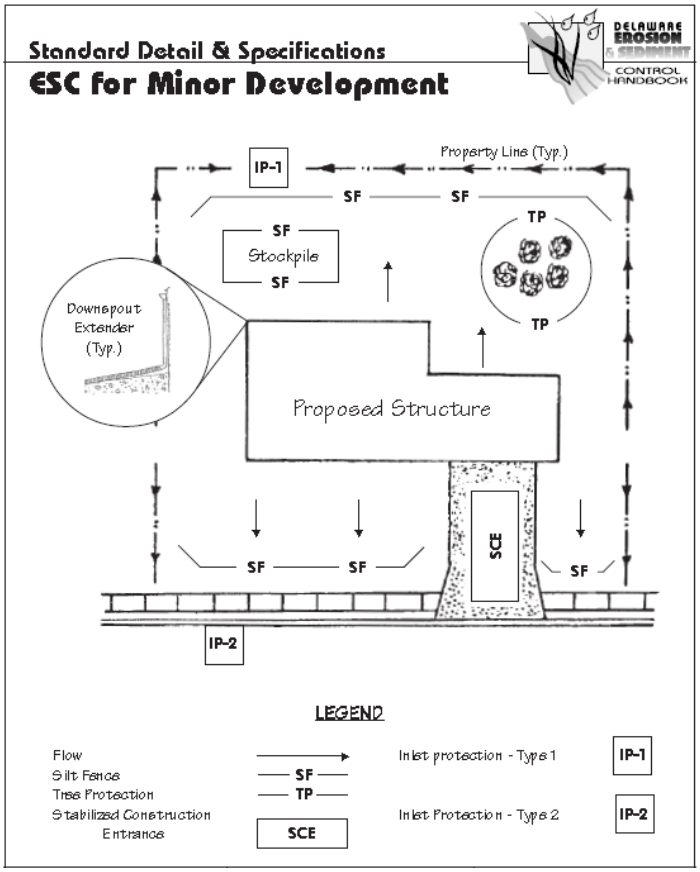

Stabilization Conditions

1. Following initial soil disturbance or redisturbance, temporary or permanent stabilization with seed and mulch shall be completed within 14 calendar days to the surface of all disturbed areas not actively under construction.
2. Specific stabilization recommendations may be found in the Delaware Erosion and Sediment Control Handbook, 3.4.3 Standard and Specifications for Vegetative Stabilization.
